



DHS NCR Consolidation

Program Update

SAME NoVA Post Program, April 4, 2019

For Official Use Only







Description:

General Overview

Original Plan (October 2006):

- Consolidate from 50 plus headquarters locations into 7 major "anchor" locations
- St. Elizabeths developed in 3 large phases; Completed in 2016
- GSA TAPS Analysis indicated consolidating 4.5 M SF at St. E's would result in a net present value savings (cost avoidance) of \$743 M over 30 years.
- Accommodate explosive growth within the Department
- Prospectus lease to consolidate Mission Support

Revised Baseline Plan (June 2013):

- St. Elizabeths developed via smaller severable segments;
 Completion extended to 2026
- Consolidate like functions into nodes to reduce locations
- No growth; No funding for Mission Support lease
- Leverage flexible workplace strategies to increase utilization

Enhanced Plan (February 2015):

- Four independently funded segments; completed in 2021
- Smaller DHS Collocated Operations Centers (DOC A only)
- Components remain intact to the extent possible
- Leverage telework and other mobile work policies to reduce construction and rent costs
- Reconfigured Munro Building (house 40% more employees)
- Reduced space standards in compliance with Freeze the Footprint goals equals reduced construction

Revision to the Enhanced Plan (also called Plan B)

- Lack of FY17/FY18 funding and lessons learned from Center Building renders the Enhanced Plan no longer viable as envisioned
- Certain leases require replacement and future St. Elizabeths development must focus on new construction
- GSA revising Master Plan, with final Master Plan and NEPA requirements complete July 2020.
- Focus 3 new construction buildings





DHS HQ Locations

Current


- 1310 N. Courthouse Rd. (NPPD)
- 1550 Wilson Blvd. (NPPD)
- 1616 N. Ft. Myer Dr. (NPPD)
- 4200 Wilson Blvd. (NPPD)
- 800 N. Capitol St. NW (NPPD, FPS)
- 1401 S. Clark St. (NPPD)
- 4601 N. Fairfax Dr. (NPPD)
- 131 M St. NE (USCIS, CRCL)
- 2121 Crystal Dr. (USCIS)
- 633 3rd St. NW (USCIS)
- 1200 1st St. NE (USCIS)
- 111 Massachusetts Ave. NW (USCIS)
- 500 C St. SW (FEMA)
- 400 C St. SW (FEMA)
- 1900 Oracle Way (TSA)
- 6354 Walker Lane (TSA)
- 601 12th St. (TSA)
- 701 12th St. (TSA)
- · EDS Dr. (TSA)

- 3801 Nebraska Ave. NW (NAC)
- 2701 Martin Luther King Jr. Ave. SE (STE)
- 950 L'Enfant Plaza SW (USCG)
- 950 H St. NW (USSS HQ)
- 940 H St. NW (USSS Webster School)
- 1100 L St. NW (USSS)
- 1300 Pennsylvania Ave. NW (CBP)
- 1301 Pennsylvania Ave. NW (CBP)
- 1400 L St. NW (CBP)
- 1717 H St. NW (CBP)
- 1901 S. Bell St. (ICE) + (CBP)
- 500 12th St. SW (ICE)
- 2451 Crystal Dr. (ICE)
- 1201 Maryland Ave. SW (ICE)
- 90 K St. NE (MGMT, ICE, I&A, CBP)
- 1201 New York Ave. NW (MGMT)
- 650 Massachusetts Ave. NW (MGMT)
- 301 7th St. SW (MGMT)
- 1801 L St. NW (DNDO)
- 1125 15th St. NW (DNDO)
- 1120 Vermont Ave. NW (S&T, OHA)


Future

- 2701 Martin Luther King Jr. Ave. SE ST Es (HQ / USCG/OSEM/CISA/ I&A / ICE or FEMA)
- 950 L'Enfant Plaza SW (USCG)
- 950 H St. NW (USSS HQ)
- 90 K St. NE (MGMT, ICE, I&A, CBP)
- 1300 Pennsylvania Ave. NW (CBP)
- 1301 Pennsylvania Ave. NW (CBP)
- MGMT/S&T –Long-term TBD
- 301 7th St. SW (MGMT Interim)
- 6595 Springfield Ctr. Dr. (TSA Future HQ)
- 1 Capital Gateway Dr. (USCIS Future HQ)
- TBD: FEMA or ICE HQ

NCR Overview Activities Underway or Completed

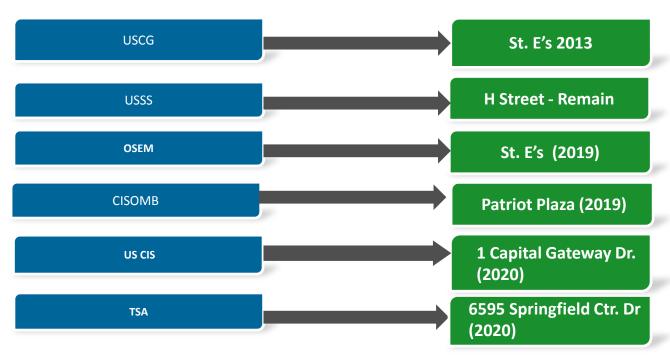

Draft NCR/St. E's Master Plan Revision Overview

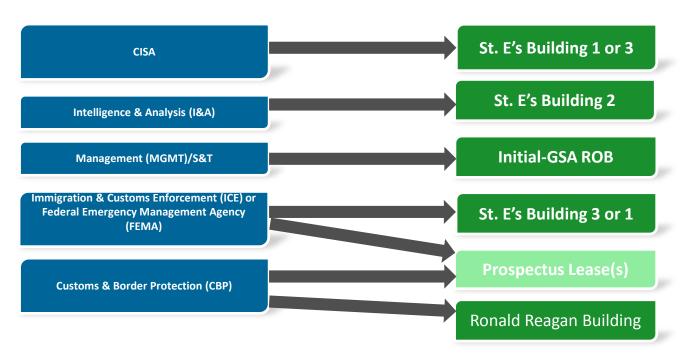


St. Elizabeths West Campus





New Construction Options

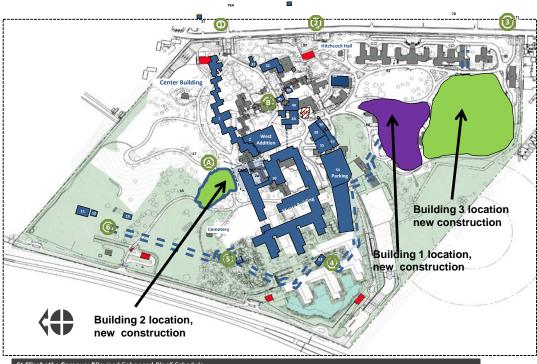

St Elizabeths Campus: "Revised Enhanced Plan" Schedule



Master Plan Concept**

New Construction Targets:

- 175K GSF on Ballfield
 - I&A
- 1.2M GSF on Plateau
 - 630K CISA
 - 570K ICE or FEMA
- 1.375M GSF: Total

** Draft Campus Map for illustrative purposes; consultation not complete.





Center Building – Future DHS HQ

In April 2019, the following HQ Offices will transition to St. E's:

- Office of the Secretary/Deputy Secretary
- Office of the Executive Secretary
- Under Secretary for Management Front Office
- Office of the General Counsel
- Office of Public Affairs
- Office of Legislative Affairs
- Office of Operations Coordination
 - Office of Partnership and Engagement
- Office of Policy
- Office of the Chief Security Officer, Technical Operations Branch
- Office of the Military Advisor
- Office of Intelligence and Analysis –Interim Front Office









National Operations Center (NOC) Relocation to St. Elizabeths (DOC A)





NOC Watch

Collaboration Center

NOC watch went live March 18th




West Addition to the Center Building





Final Design Rendering

West Addition



Move second/third quarter FY20



11



Munro Building





- USCG Headquarters is about 1.3 M square feet
- Originally designed for 3,700 employees based on prior standards and traditional 1:1 seating
- Munro Optimization will add additional DHS occupancies (CWMD) by adopting flexible workplace strategies, new and smaller space standards
 - CWMD to be provided up to 540 seats
 - Allows for anticipated USCG growth in alignment with original seats envisioned
 - Funded using FY16 MGMT Appropriations
 - Cost Estimate \$30,000,000
 - Full Operational Capability Late 2021 / Early 2022



Hitchcock Hall





- Historic full featured performance auditorium for patient entertainment and treatment. Upended in 1912
- Originally planned/funded for renovation during phase 1 but de-scoped by GSA during construction due to funding shortfalls.
- Adaptive reuse as a training, conference and meeting space. Will seat 600+ in the main auditorium.
- Two smaller conference rooms and a television studio are included in the build-out.
- Construction will complete June/July 2019.
 Information technology installations will continue until the end of 2019.



FOUO



Transportation

- Extend Access Road from Gate 4 to Malcolm X Ave and reconstruct the I-295/South Capital Streel/Malcolm X Interchange
- GSA funded \$144 million in FY 2015 appropriation
- District of Columbia Department of Transportation (DDOT) to execute project on behalf of and in coordination with GSA
- DDOT awarded construction contract, construction in progress.
- Completion estimated late 2021-2022





Questions?

